

Development Update - Infrastructure, amenities and facilities at Netherton Grange

We take pride in what we do and work hard to deliver developments our customers will enjoy living in.

As well as building high quality homes, our developments are designed to include the necessary infrastructure, useful amenities, leisure facilities and green open spaces.

The table below gives details of the works which are in progress and are planned to be delivered at Netherton Grange. The works are also shown on the plan below.

The timescales provided for completion of works are indicative and may be subject to change based on external market factors.

For information on progress of these works please check the Development website accessed via www.crestnicholson.com

Schedule of Remaining Works to Parcel

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
1	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	No	Complete Q4 2026 Q4 2026
2	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	No	Complete Q3 2026 Q3 2026
3	Private Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	No	Complete Q3 2026 Q3 2026
4	Private Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	No	Complete Q3 2026 Q3 2026
5	Private Road	Complete road constructionComplete final surfacing	No	Complete Q4 2025



Development Update - Infrastructure, amenities and facilities at Netherton Grange

		Complete remaining highway landscaping		Complete
6	Adoptable Road	Complete road construction	No	Complete
		Complete final surfacing		Q4 2026
		Completion of remaining highway landscaping		Q4 2026
7	Private Road	Complete road construction	No	Q3 2026
		Complete final surfacing		Q1 2027
		Completion of remaining highway landscaping		Q3 2026
8	Private Road	Complete road construction	No	Q3 2026
		Complete final surfacing		Q1 2027
		Completion of remaining highway landscaping		Q3 2026
9	Adoptable Road	Complete road construction	No	Complete
		Complete final surfacing		Q1 2027
		Completion of remaining highway landscaping		Q4 2026
10	Private Road	Complete road construction	No	Complete
		Complete final surfacing		Q4 2026
		Complete remaining highway landscaping		Q4 2026
11	Adoptable Road	Complete road construction	No	Complete
		Complete final surfacing		Q1 2027
		Complete remaining highway landscaping		Q4 2026
12	Private Road	Complete road construction	No	Q1 2026
		Complete final surfacing		Q1 2027
		Complete remaining highway landscaping		Q4 2026
13	Private Road	Complete road construction	No	Q1 2026
		Complete final surfacing		Q1 2027
		Complete remaining highway landscaping		Q4 2026
14	Public Open Space	Complete tree planting in relevant seasonal window following	No	Complete
		the completion of surrounding hardstanding.		



Development Update - Infrastructure, amenities and facilities at Netherton Grange

		Complete grass seeding in upcoming seasonal seeding window		Complete
15	Public Open Space	 Complete tree planting in relevant seasonal window following the completion of surrounding hardstanding. Complete grass seeding in upcoming seasonal seeding window 	No	Q2 2026 Q2 2026
16	Attenuation Pond	 Complete attenuation pond Complete planting / grass seeding in upcoming seeding window 	Yes	Complete Complete


Notes:

• The estate management company will also be responsible for maintaining small areas of incidental landscaping and shared drive accesses for a small number of properties. These items are not included on the above schedule due to their more limited nature and use, however they will be completed alongside the adjacent homes.



Development Update - Infrastructure, amenities and facilities at Netherton Grange

Parcel Remaining Works Plan

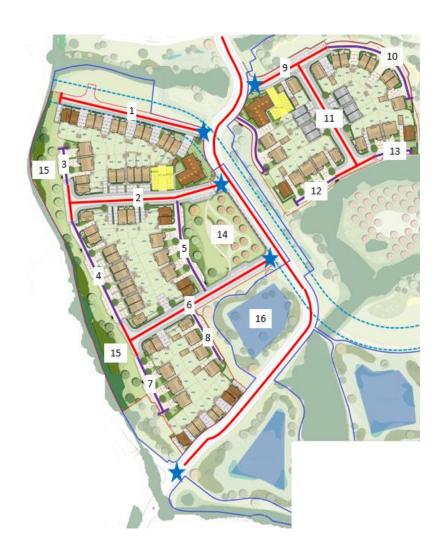



Development Update - Infrastructure, amenities and facilities at Netherton Grange

Schedule of Wider Estate Remaining Works

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
1	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	Yes	Complete Complete Complete
2	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	Yes	Q1 2027 Q1 2027 Q1 2027
3	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	Yes	Complete Complete Complete
4	Adoptable Road	 Complete road construction Complete final surfacing Complete remaining highway landscaping 	Yes	Complete Q1 2027 Q1 2027
5	Attenuation Pond	 Complete attenuation pond Complete planting / grass seeding in upcoming seeding window 	Yes	Complete Complete
6	Attenuation Pond	 Complete attenuation pond Complete planting / grass seeding in upcoming seeding window 	Yes	Complete Complete
7	Equipped Play Area (LEAP)	Complete installation of Play equipment	Yes	Complete
8	Equipped Play Area (NEAP)	Complete installation of Play equipment	Yes	Q1 2027
9	Allotments	Complete allotments	Yes	Q2 2027



Development Update - Infrastructure, amenities and facilities at Netherton Grange

Wider Estate Remaining Works Plan





Development Update - Infrastructure, amenities and facilities at Netherton Grange

Managing Agent Contact Details

Netherton Grange Management Company has appointed Firstport to undertake the estate management for the development. Should you wish to discuss any estate management matters please contact the following:

T: 0333 321 4080 **Web**: <u>www.firstport.co.uk</u>
