



Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

We take pride in what we do and work hard to deliver developments our customers will enjoy living in.

As well as building high quality homes, our developments are designed to include the necessary infrastructure, useful amenities, leisure facilities and green open spaces.

The table below gives details of the works which are in progress and will be delivered at Malabar, Daventry. The works are also shown on the plan below.

The timescales provided for completion of works are indicative and may be subject to change based on external market factors.

For information on progress of these works please check the Development website accessed via www.crestnicholson.com



CREST
NICHOLSON

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Schedule of Remaining Works to Parcel

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
1	Adoptable Spine Road	Complete final surfacing	YES	Q3 27
2	Adoptable Road	Complete final surfacing	NO	Complete
3	Private Road	Complete final surfacing	NO	Q3 27
4	Adoptable road	Complete final surfacing	NO	Complete
5	Private Road	Complete final surfacing	NO	Complete
6	Private Road	Complete final surfacing	NO	Complete
7	Private Road	Complete final surfacing	NO	Complete
8	Private Road	Complete final surfacing	NO	Complete
9	Private Road	Complete final surfacing	NO	Complete
10	Adoptable Road	Complete final surfacing	NO	Complete
11	Adoptable Road	Complete final surfacing	NO	Q3 27

October 2026 – Updated Quarterly



CREST
NICHOLSON

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
12	Private Road	Complete final surfacing	NO	Complete
13	Private Road	Complete final surfacing	NO	Q3 27
14	Private Road	Complete final surfacing	NO	Complete
15	Private Road	Complete final surfacing	NO	Complete
16	Private Road	Complete final surfacing	NO	Q3 27
17	Private Road	Complete final surfacing	NO	Q3 27
18	Parking Courts	Tarmac surface course to roadway within parking court	NO	Q3 27
19	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 27
20	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 27
21	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 27
22	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 27

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
23	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q2 27
24	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q2 27
25	Equipped Play Area	Install play equipment and open play area	YES	Complete
26	Adoptable Road	Complete final surfacing	YES	Q4 29
27	Parking Courts	Tarmac surface course to roadway within parking court	NO	Q4 29
28	Parking Courts	Tarmac surface course to roadway within parking court	NO	Q4 29
29	Drainage Basin	Install Drainage basin	YES	Q4 29
30	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 29

Notes:

- The estate management company will also be responsible for maintaining small areas of incidental landscaping and shared drive accesses for a small number of properties. These items are not included on the above schedule due to their more limited nature and use, however they will be completed alongside the adjacent homes.



CREST
NICHOLSON

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Parcel Remaining Works Plan



Plots 126-172



Plots 1-125

October 2026 – Updated Quarterly

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Schedule of Remaining Works to Wider Estate

Plan Ref	Description	Remaining Works	Is a Third Party Responsible for Completing?	Forecast Date for Works Completion
1	Adoptable Road	Complete final surfacing along spine road	YES	Q4 29
2	Adoptable Road	Complete final surfacing of new roundabout onto A45	YES	Complete
3	Pumping Station	Install and commission pumping station	YES	Complete
4	Public Open Space	All public open space works to be completed including hard and soft landscaping	YES	Q4 31




CREST
NICHOLSON

Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Wider Estate Remaining Works Plan

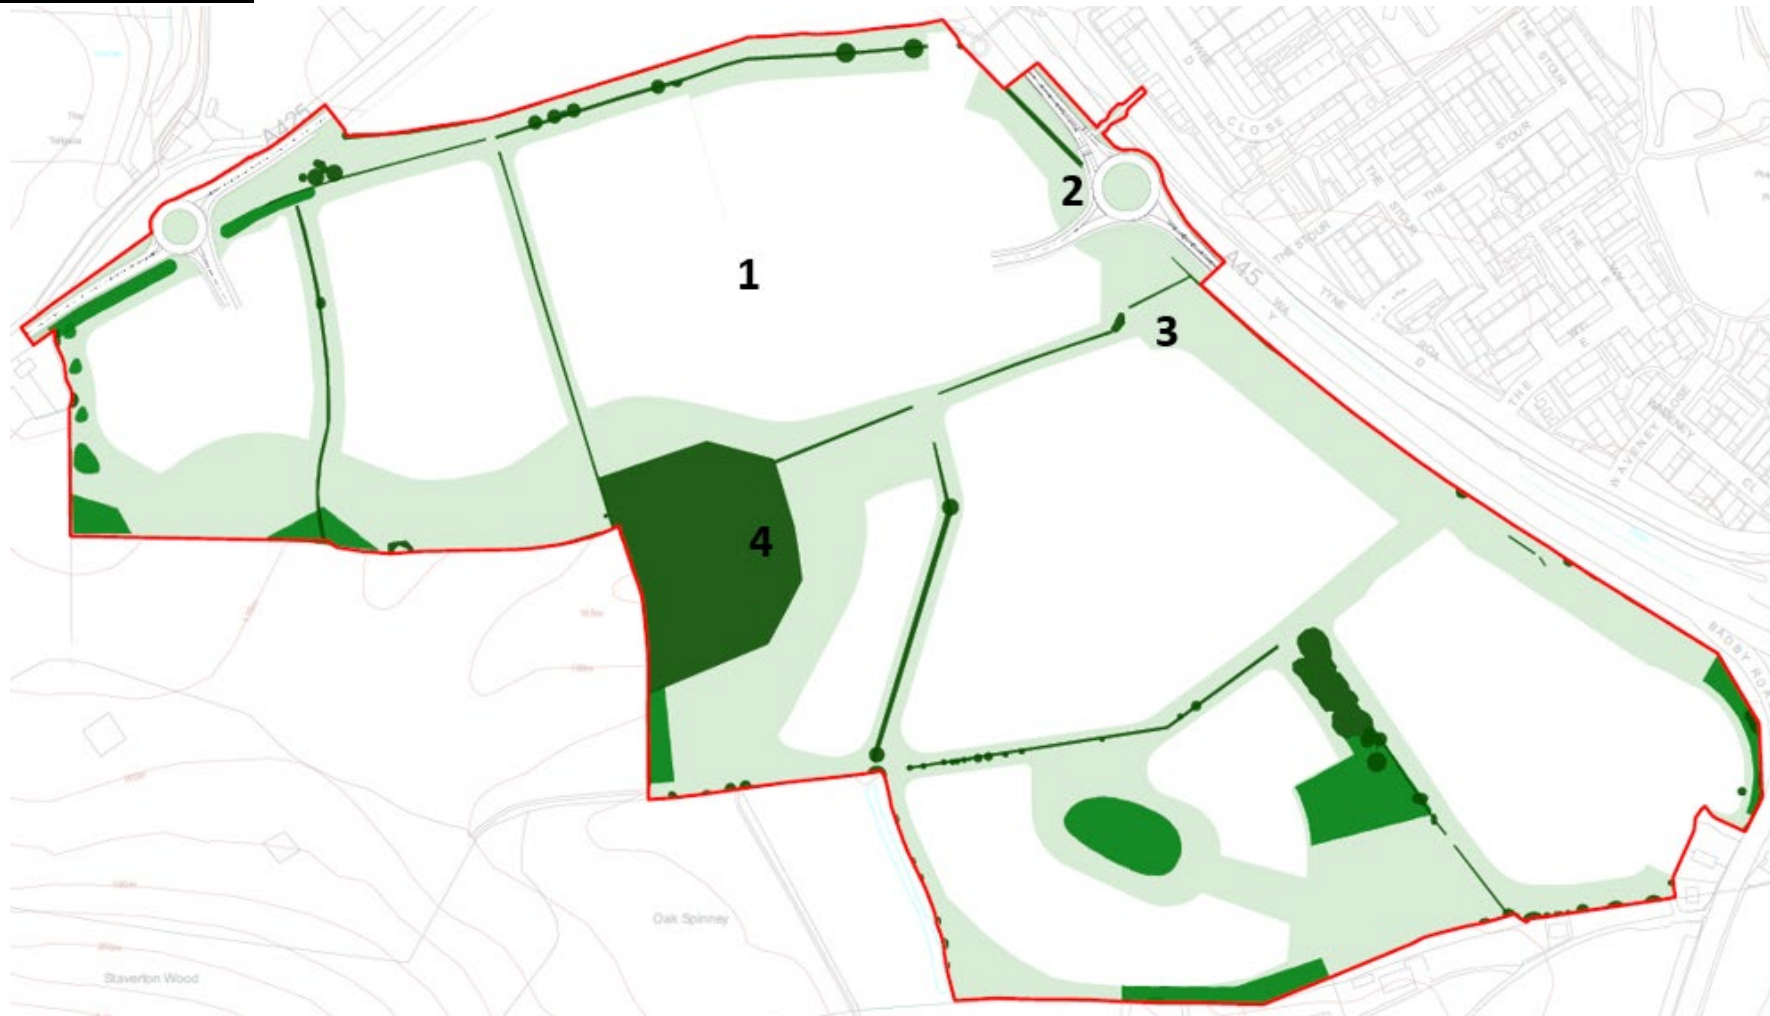

October 2026 – Updated Quarterly



Building Great Places

Development Update - Infrastructure, amenities and facilities at Malabar, Daventry

Managing Agents Contact Details

Crest Nicholson has appointed **Centrick** to undertake the estate management for the development. Should you wish to discuss any estate management matters please contact the following:

Centrick
The Exchange,
19 Newhall Street,
Birmingham,
B3 3PJ
0121 289 4422
estate@centrick.co.uk
